EDUCATIONAL DEMO · SYNTHETIC DATA ONLY · NOT A CLINICAL PRODUCT

Samvad HealthDesk AI Final Release Certification Report

Backend remediation, branch integration, audio generation readiness, Supabase/Vercel preparation and combined regression

48	4	3	0	30/0
DEFECTS FIXED	OWNER ACTIONS	VISUAL OPEN	P0/P1 OPEN	RELEASE GATE

Certified for owner-supervised deployment. All executable gates pass, including a real local Supabase stack (55/55 API, 52/52 integration, 209/209 emergency, 47 SQL assertion blocks). Not yet approved for public evaluator access.

Two blockers are owner actions, not code defects: the shipped prompt audio is digital silence, and decisions D-30 / D-34 are unrecorded. Three cosmetic visual items remain open. Hosted Supabase, Vercel and live providers were not exercised.

Report date	3 November 2026
Release candidate	`release-candidate/samvad-final` @ `b6ee111`
Frontend	`feat/frontend-figma-parity` @ `a8a3cf6`
Backend	`feat/backend` @ `e5d77e5`
Audit baseline	`audit/final-ui-logic-figma-review` @ `ab4ba5b`
Disposition	Candidate is disposable and unmerged. Nothing was deployed.

1. Executive release decision

The candidate integrates the backend feature work, the design owner's committed visual pass and the OpenCode remediation into one reproducible tree, and for the first time verifies the backend against a **real local Supabase stack**: real Auth, real JWTs, real RLS, real Edge Functions and a real PostgreSQL database, with providers served by a local stub.

> **Unified release gate: 30 PASS · 0 FAIL · 0 BLOCKED · 0 NOT TESTED.** The previously blocked `test:api` suite now runs and passes 55/55.

Verdict: certified for owner-supervised deployment. **Not** approved for public evaluator access until the prompt audio is real, the two owner decisions are recorded, the hosted smoke test is run and the five open visual findings are accepted or fixed.

Gate	Verdict
Internal scripted demo (real local stack)	PASS
Owner visual acceptance	CONDITIONAL 3 cosmetic items open
Security / RLS / authorization	PASS real stack
Hosted Supabase readiness	PASS procedure ready; 5 owner-blocked preflight items
Vercel readiness	PASS verified, no secrets in client vars
Hosted smoke test	NOT TESTED owner credentials required
Live provider behaviour	NOT TESTED no credential used
Public evaluator access	NOT YET audio + decisions + hosted smoke

2. Commit matrix

Role	Ref	Commit	Integration
Frontend (design owner)	feat/frontend-figma-parity	`a8a3cf6`	merged
Backend	feat/backend	`e5d77e5`	base
Emergency certification	feat/emergency-certification-v3	`b913506`	merged
Speech round-trip (+ provider harness)	feat/speech-roundtrip-verification-v2	`13e88b2`	merged (includes `0cff52a`)
Question-bank integrity	feat/question-bank-integrity	`37cf711`	merged
Demo lifecycle ops	feat/demo-lifecycle-ops	`d6e7551`	merged
Doctor conversation reader	feat/doctor-conversation-reader	`5e584b5`	already an ancestor
OpenCode remediation	fix/opencode-audit-frontend	`c12df34`	already an ancestor
Prompt audio (new)	fix/opencode-prompt-audio	`5ef0086`	merged
Backup-restore tooling (new)	fix/opencode-backup-restore	`cbf1d0d`	merged
Release candidate	release-candidate/samvad-final	**`b6ee111`**	disposable, unmerged

3. Integration history

1. Base `e5d77e5`; merged emergency certification (2 commits).
2. Merged speech round-trip (brings the provider harness). Conflict: generated `release-check-result.json` only.
3. Merged question-bank integrity; conflicts limited to generated result JSONs.
4. Provider harness: already contained, no-op. Merged demo lifecycle ops (generated JSON conflicts only).

5. Merged the design owner's branch. Conflicts: `.env.example` (kept the superset with both public and server-secret names) and two docs (kept the fuller versions).
6. OpenCode remediation was already an ancestor, so it was not merged twice.
7. Corrective commit `01730a8` (N-05), then merged the prompt-audio and backup-restore branches.
8. Merged the design owner's follow-up (`3574e23` / `a8a3cf6`) — processing, booking, review, reports-list and slot-state screens; only screenshot binaries conflicted.
9. Merged `fix/opencode-hindi-copy` (`88964b0`) closing the remaining English strings.

Excluded deliberately: `release/rc-1`, `release/samvad-rc1`, `feat/frontend`, `feat/frontend-integration`, `feat/foundation`, `main` (older or superseded), and the superseded emergency/speech revisions.

4. Figma visual acceptance

22 frames and 16 exported vectors remain the baseline. Closed in the candidate: the mic-denied and processing screens, the booking layout (3 date chips + More dates, timed CTA, no doctor card), the review row layout, the reports list, the dedicated no-slot state, the 92 px confirmation with a report-sent note, password reveal, chip selection and the last hardcoded English strings on patient screens. **Three cosmetic items remain open**: the avatar white containers (D-43/D-44) and the brand-plus metrics (D-45). Visual acceptance is conditional on the owner accepting those three.

5. Screen, icon and component audit

12 patient and 8 doctor components; two Edge Functions; eleven migrations. Only `src/lib/api.ts` touches Supabase. Report v1.2 statuses are preserved. No fixture router or synthetic report table exists in `src/`. Adopted Figma vectors: sidebar icons, assistant/patient avatars, pencil, paper-plane, check circle. Open: avatar containers (D-43/D-44), brand plus (D-45), a few rounded-square icons.

6. Buttons and navigation

Forward flow, Back on non-terminal screens, terminal guards on emergency and both confirmations, doctor list ↔ detail with preserved search/tab, logout, direct `/doctor` while logged out. Previously inert controls now work or report honestly. Inventory: 6 controls, 0 unlabelled, 0 dead links, 100% accessible names.

7. Patient workflow

Real stack: anonymous auth → consent → fixed questions → adaptive bank-v2 questions → draft → correction → submit → slots → booking → confirmation. Hindi journey end to end. Emergency path separate. `demo_busy` exercised by exhausting the local cap.

8. Doctor workflow

Login requires a mapped identity; an unmapped Auth user is signed out. Dashboard, reports, detail with real warning flags, stored conversation, Mark Reviewed (timestamp and reviewer only), appointments, urgent queue. General Medicine reads emergency reports; only the Emergency doctor acknowledges.

9. Emergency certification

209/209 on the candidate: matcher scoping (multiple occurrences, clause boundaries, negation window), deterministic rule order, fixed clarification, live escalation matrix, doctor authorization, logging privacy, question-bank and phrase hash invariants. 112 is plain text; no slots; no Back control.

10. Microphone and recording

12-case lifecycle suite passes (start after permission, wall-clock 30 s, hard stop, idempotent stop, track release, WAV re-encode, transcript preview, no silent re-capture). **Physical microphones and real device browsers were not exercised.**

11. English/Hindi speech

Mocked round-trip harness 25/25: Unicode-safe comparison, punctuation/whitespace tolerance, mismatch detection, timeout and error paths, four-request budget, non-live default. **Live TTS→STT was not run** and is not clinical accuracy validation.

12. Consent audio assets

Check	Result
Cached-first resolution	PASS .mp3 then shipped .wav
Provider call for a fixed prompt	PASS none (E2E asserted)
Autoplay-blocked vs missing asset	PASS two distinct states
Adaptive replay caching	PASS one call per language+question
Shipped files contain speech	FAIL 11 × 1.000 s, -91 dB, byte-identical
Generator ready	PASS dry-run default, double opt-in, silence/duplicate checks

13. Appointment and booking

14-day IST weekday slots; atomic reservation; duplicate slot and duplicate report refused; cross-patient read/booking refused; emergency permanently ineligible; flagged reports held until review. Confirmation renders a real IST date and time (captured). A slot id is rejected as a timestamp.

14. Doctor conversation reader

Stored patient answers only, chronological, transcript vs confirmed text and input mode, RLS-scoped, drafts never visible. Verified on the real stack.

15. Authentication and RLS (real local stack)

#	Check	Result
1	Anonymous patient authentication	PASS
2	Session creation and ownership	PASS
3	Report submission	PASS
4	Message insertion	PASS
5	Doctor authentication	PASS
6	Doctor ↔ profile mapping (refuses unmapped)	PASS
7	Assigned General Medicine access	PASS
8	Emergency cross-visibility	PASS
9	Emergency-only acknowledgement	PASS
10	Cross-department rejection	PASS
11	Report immutability + draft invisibility	PASS
12	Appointment booking	PASS
13	Duplicate appointment rejection	PASS
14	Unauthenticated / invalid JWT	PASS (clock expiry not simulated)
15	Edge Function authorization	PASS

#	Check	Result
16	Consent persisted with version and text	PASS

16. Supabase setup readiness

`docs/release-readiness/HOSTED-SUPABASE-SETUP.md`: 14 ordered owner steps with exact commands — project, ref, 11 migrations, seed, two Auth users, mapping, three secrets, both function deploys, JWT check, exact CORS origin, hosted smoke list, RLS checks, workflow checks, rollback.

17. Vercel setup readiness

`docs/release-readiness/VERCEL-DEPLOYMENT.md`: verified build command and output, SPA rewrite, public-only `VITE_` variables, preview/production separation, origin allowlisting, 12-step smoke list, rollback by promoting the previous deployment.

18. Complete defect register (55 findings)

The original 50 findings keep their IDs; N-01…N-05 were raised during the remediation and certification rounds (55 findings in total). 48 fixed/verified · 4 owner action · 3 open (all visual). No P0 or P1 defect remains open; the four owner actions are the prompt audio (D-06/N-02), D-30 and D-34.

ID	Sev	Finding	Status	Evidence / implementation
D-01	P0	Doctor warning flags hardcoded to None	FIXED	Data-driven flags, 4 states, 11 tests, captured urgent detail
D-02	P1	Back on emergency restores routine intake	FIXED	Terminal state + no Back control + E2E assertion
D-03	P1	Confirmation shows Invalid Date	FIXED	ISO slot_start, IST formatter, captured confirmation
D-04	P1	demo_busy ignored at session start	FIXED	Busy notice + retry + disabled consent
D-05	P1	Mic-denied screen missing	FIXED	Real state, text fallback, retry
D-06	P1	No cached greeting; paid replay per click	OWNER ACTION	Caching/guard fixed; shipped audio is silence
D-07	P1	Hindi emergency body in English	FIXED	t.emergency.guidance + notice
D-08	P1	Production fixtures / credential-free doctor	FIXED	Deleted from src; scan test; bundle clean
D-09	P2	Processing screen not a real state	FIXED	Real processing view wired to isProcessing
D-10	P1	Back from confirmation re-opens booking	FIXED	Terminal + read-only summary + duplicate refusal
D-11	P1	Back to consent resets intake	FIXED	Idempotent consent; state restored
D-12	P1	other_symptoms not correctable	FIXED	Row + multi-value editor
D-13	P2	Try another date does nothing	FIXED	Next date with a free slot
D-14	P2	All absences shown as Not provided	FIXED	Six distinct status labels
D-15	P2	Missing information recomputed	FIXED	Reads report.missing_information
D-16	P2	Booking layout differs from Figma	FIXED	3 date chips + More dates, timed CTA, no doctor card
D-17	P2	Fixture dashboard/list mismatch	FIXED	Single data source; computed badges
D-18	P2	Appointment headers mismatch cells	FIXED	Relabelled Department / Reference
D-19	P2	Play question again navigates away	FIXED	Replay handler wired
D-20	P2	No More dates control	FIXED	14-day window control
D-21	P2	Browser-timezone slot times	FIXED	Explicit Asia/Kolkata formatting
D-22	P2	Slot load error looks like no slots	FIXED	Distinct error state + retry
D-23	P2	Silent session loss on refresh	FIXED	Explicit restore-failure message
D-24	P2	Hidden links are the first tab stops	FIXED	Removed from tab order
D-25	P2	Doctor load errors swallowed	FIXED	Loading/error/retry, last good data kept
D-26	P2	Hardcoded English on patient screens	FIXED	All listed strings localized; E2E enforces it
D-27	P3	No password reveal	FIXED	Eye toggle
D-28	P3	No in-flight disabling	FIXED	Submit/Book/Edit disabled while pending
D-29	P2	Reports filter state lost on Back	FIXED	Tab/search lifted to the shell
D-30	P2	Urgent review authority ambiguity	OWNER ACTION	Fail-closed: Emergency doctor only (UI + RPC)
D-31	P2	Review row layout differs	FIXED	Label column + value + pencil
D-32	P2	Reviewed-by name hardcoded	FIXED	Resolved via reviewed_by

ID	Sev	Finding	Status	Evidence / implementation
D-33	P2	Source chip hardcoded	FIXED	Derived from report + input modes
D-34	P2	Consent bubble copy divergence	OWNER ACTION	Decision documented, not changed
D-35	P2	Urgent detail content hardcoded	FIXED	Report data + routing snapshot
D-36	P3	canReview fails open	FIXED	Deny by default
D-37	P2	Submitted report shown as draft	FIXED	Read-only submitted summary
D-38	P3	Language choice not persisted	FIXED	localStorage + documentElement.lang
D-39	P2	Conversation dead end	FIXED	Explicit panel with End
D-40	P3	Silent microphone re-capture	FIXED	Reported, never re-records
D-41	P3	Navigate before answer accepted	FIXED	Await then navigate
D-42	P3	Appointments default to Today	FIXED	Upcoming default
D-43	P2	Assistant avatar glyph/container	OPEN	Exact vector adopted; container remains
D-44	P2	Patient avatar glyph/container	OPEN	Exact vector adopted; container remains
D-45	P3	Brand plus metrics	OPEN	Unchanged (cosmetic)
D-46	P3	Gender prints lower-case	FIXED	Capitalised / mapped
D-47	P2	Reports list is a table	FIXED	Rebuilt as Figma list rows
D-48	P2	No dedicated slot-state screens	FIXED	Dedicated no-slot card + retry
D-49	P2	Confirmation layout differs	FIXED	92 px circle + report-sent note
D-50	P3	Severity chip always dark	FIXED	Selection-driven styling
N-01	P1	Branch fabricated demographics and a date	FIXED	Rejected at merge; data-driven retained
N-02	P1	Shipped prompt audio is silence	OWNER ACTION	11 files 1.000 s at -91 dB; generator ready
N-03	P2	Design corrections uncommitted	VERIFIED FIXED	Committed 78b68c2; diff byte-identical
N-04	P2	Backup-restore rehearsal not executable	FIXED	Platform baseline in scratch DB; real dump restored
N-05	P1	Lossy merge broke build and re-added fake data	FIXED	Six files restored; src identical to validated tree

19. Severity summary

Severity	Count	Fixed / verified	Owner action	Open
P0	1	1	0	0
P1	13	11	2	0
P2	31	27	2	2
P3	10	9	0	1
Total	**55**	**48**	**4**	**3**

20. Test results with execution environment

Suite	Environment	Command	Result
TypeScript	macOS local	`npx tsc --noEmit`	**clean**
Frontend mock/unit	Node 26 + tsx	`npm run test:mock`	**121/121**

Suite	Environment	Command	Result
Supabase contract (SIMULATED)	Node + tsx	`npm run test:supabase`	**7/7**
API integration — REAL local stack	Docker + CLI 3.0.0 + Edge Functions	`npm run test:api`	**55/55**
Integration harness — REAL stack	same	`deno run supabase/tests/integration.ts`	**52/52**
Adaptive harness — REAL stack	same	`deno run supabase/tests/adaptive.ts`	**33/33**
Emergency certification — REAL stack	same	`deno run supabase/tests/emergency-certification.ts`	**209/209**
SQL RLS / booking / immutability	local PostgreSQL 17.11	`8 files via psql`	**47 assertion blocks pass**
Backend Deno unit	Deno 2.9.7, mocked providers	`deno test _shared/ .`	**232/232**
Prompt-audio manifest drift	Deno	`deno test supabase/tests/prompt-audio-manifest.test.ts`	**3/3**
Speech round-trip (MOCKED)	Deno	`deno test supabase/tests/provider-roundtrip.test.ts`	**25/25**
Provider smoke (MOCKED)	Deno	`deno test supabase/tests/provider-smoke.test.ts`	**17/17**
Browser E2E	headless Chrome, built bundle	`npm run test:e2e`	**16/16**
Visual QA	headless Chrome, 7 viewports	`npm run test:visual`	**pass, 23 shots**
Production build	Vite 6	`npm run build`	**pass, 111 modules**
Unified release gate	local stack	`scripts/release-check.ts --frontend`	**30 PASS / 0 FAIL**
Deployment preflight	local	`scripts/verify-deploy-config.ts`	**17 PASS / 5 owner-blocked**
Demo preflight	local	`scripts/demo-preflight.ts`	**16/16**
Backup -> restore	local dump -> scratch DB	`scripts/verify-backup-restore.ts --execute`	**pass, then dropped**

Local stack: Supabase CLI 3.0.0, PostgreSQL 17.11, Edge Runtime 1.77.8, Docker 29.9.2. Providers were served by `supabase/tests/stub-providers.ts`; no live provider request was made. The emergency certification required temporarily raising the local session cap (100 → 500) because the suite creates many sessions; it was restored to 100 immediately afterwards.

21. Blocked, skipped and untested

- Live Groq / Prisma / Timbre and the live speech round-trip — no credential, explicit authorization required.
- Live prompt-audio generation — same; the generator is ready.
- Hosted Supabase smoke and hosted Vercel deployment — not created or deployed by instruction.
- Physical microphone, iOS/Android, Safari, Firefox, screen reader — unavailable in this environment.
- Clock-based JWT expiry — unauthenticated/invalid JWT is covered, expiry is not simulated.
- 15-turn cap in the browser — unreachable in mock mode (≤13 turns); covered by unit tests.
- Clinical speech accuracy — explicitly out of scope.

A local-stack pass is not a hosted pass; a stubbed-provider pass is not provider verification.

22. Owner actions

1. Generate the ten prompt-audio files after reserving the attempts in the daily limit, then complete the listening pass.

2. Record D-30 (urgent-review authority + urgent-queue membership).
3. Record D-34 (consent copy) and approve the Hindi consent wording.
4. Create and link the hosted project; apply migrations and seed; create and map the two doctors; set the three secrets; deploy both functions.
5. Create the Vercel project; set the two public variables and the exact origin in ALLOWED_ORIGINS.
6. Run the hosted smoke list and record the result.
7. Approve merging the candidate into the permanent release branch.

23. Deployment checklist and rollback


Before: decisions recorded · audio generated and listened to · secrets set · exact CORS origin · migrations and seed applied · two doctors mapped · preflight green · local suites green. **Order:** migrations → seed → doctor users → mapping → secrets → chat-turn → speak → Vercel env → deploy → CORS redeploy → hosted smoke. **Rollback:** promote the previous Vercel deployment; redeploy the previous functions; restore the pre-migration backup for schema failures; ban the doctor accounts or pause the project to stop public access.

24. Final recommendation


The candidate is **technically ready for owner-supervised deployment** and is the first version whose backend is verified against a real database, real JWTs, real RLS and real Edge Functions. It is **not yet ready for public evaluator access**: the prompt audio is silent, two owner decisions are unrecorded, three cosmetic visual items remain open, and neither the hosted environment nor a live provider has been exercised.

No claim of launch, production readiness or clinical validity is made. Merge, deployment and hosted setup remain owner actions.


25. Screenshot evidence

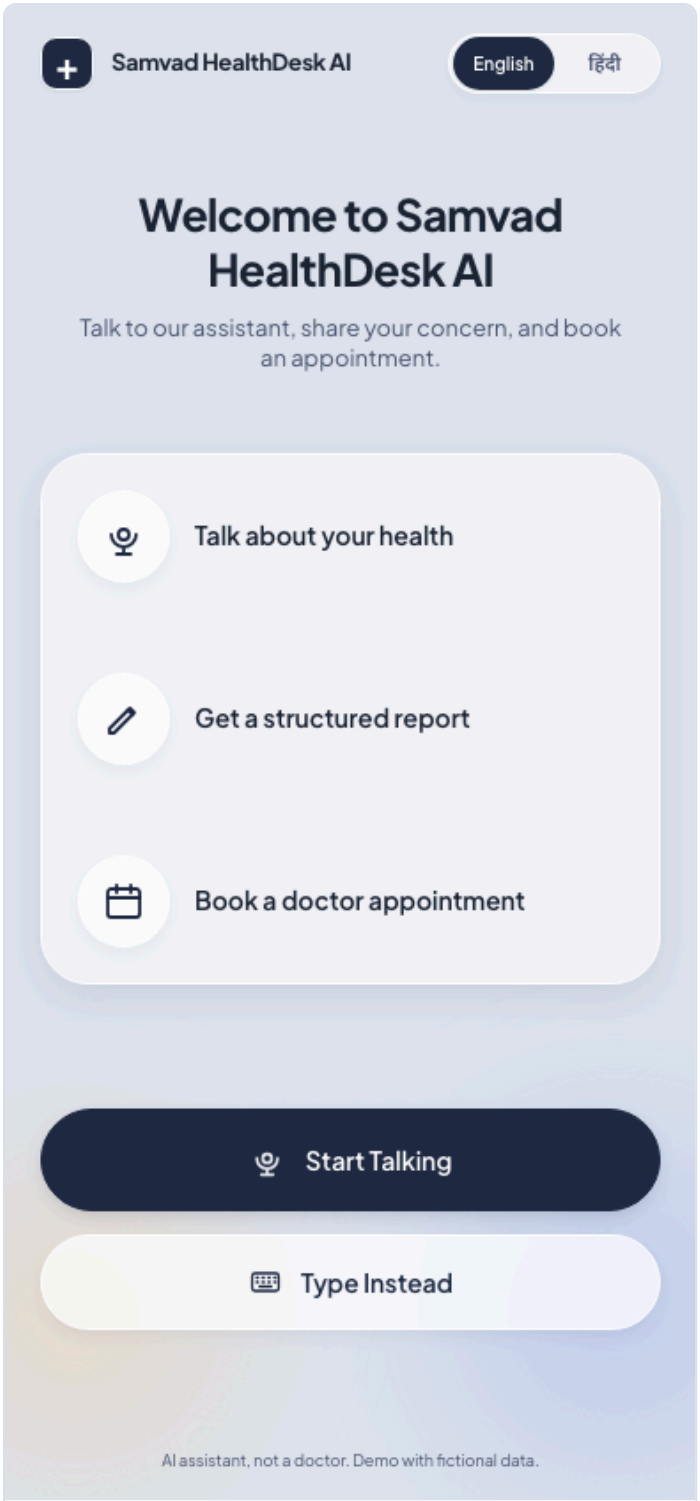


Welcome (mobile)

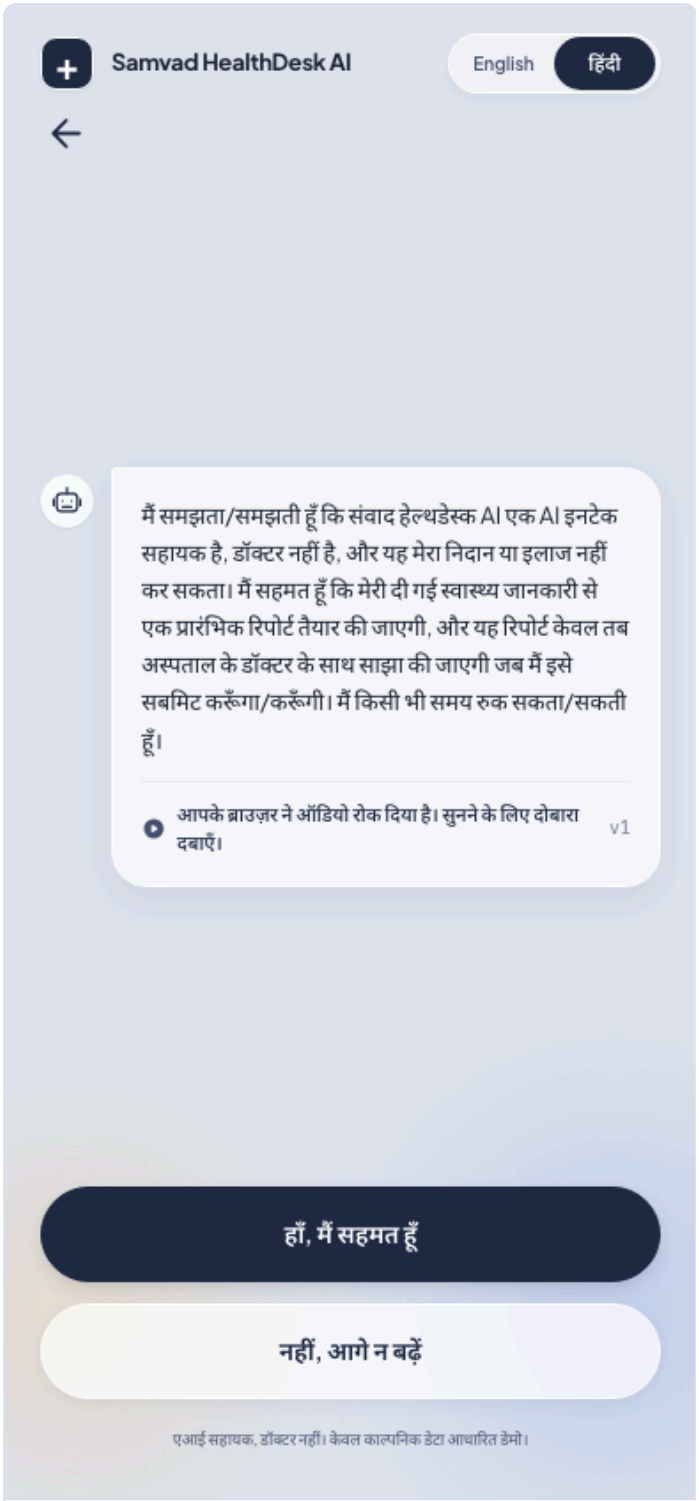


Consent + cached greeting

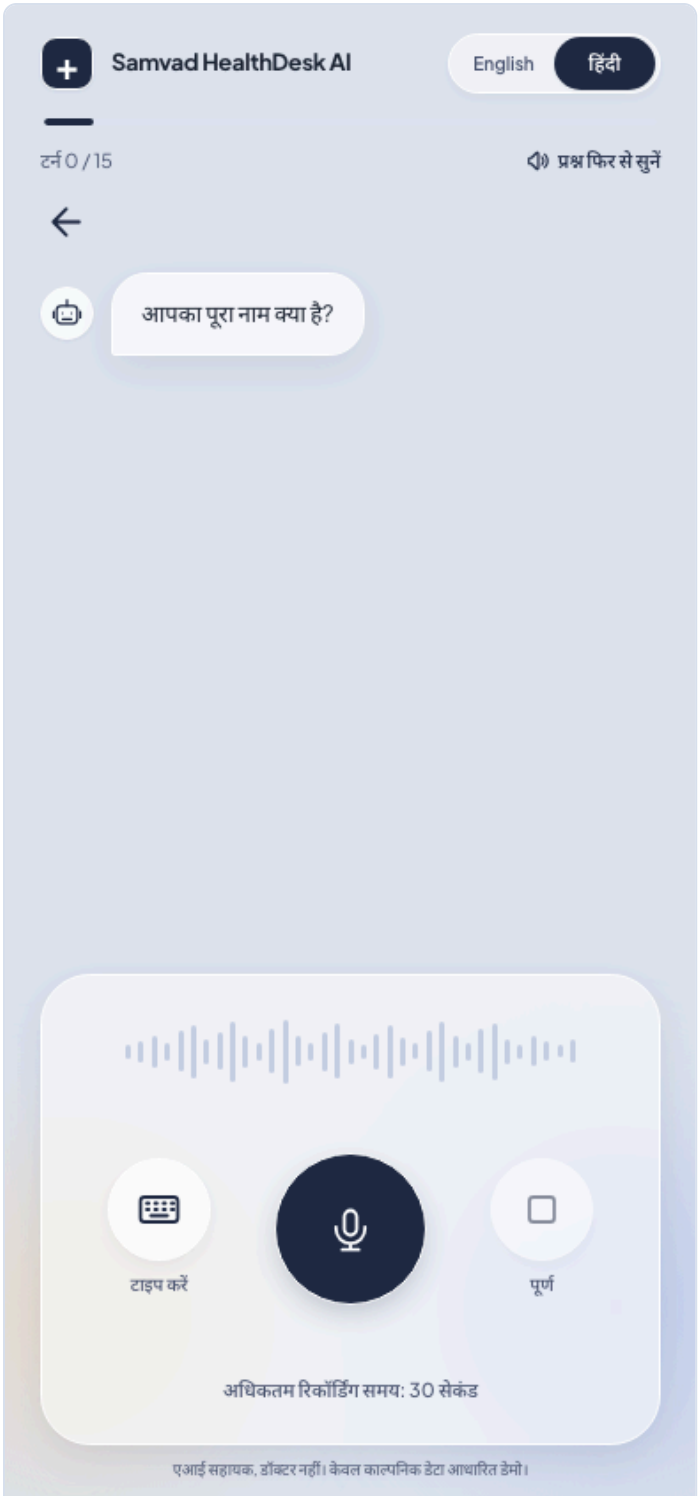


Conversation (Hindi)

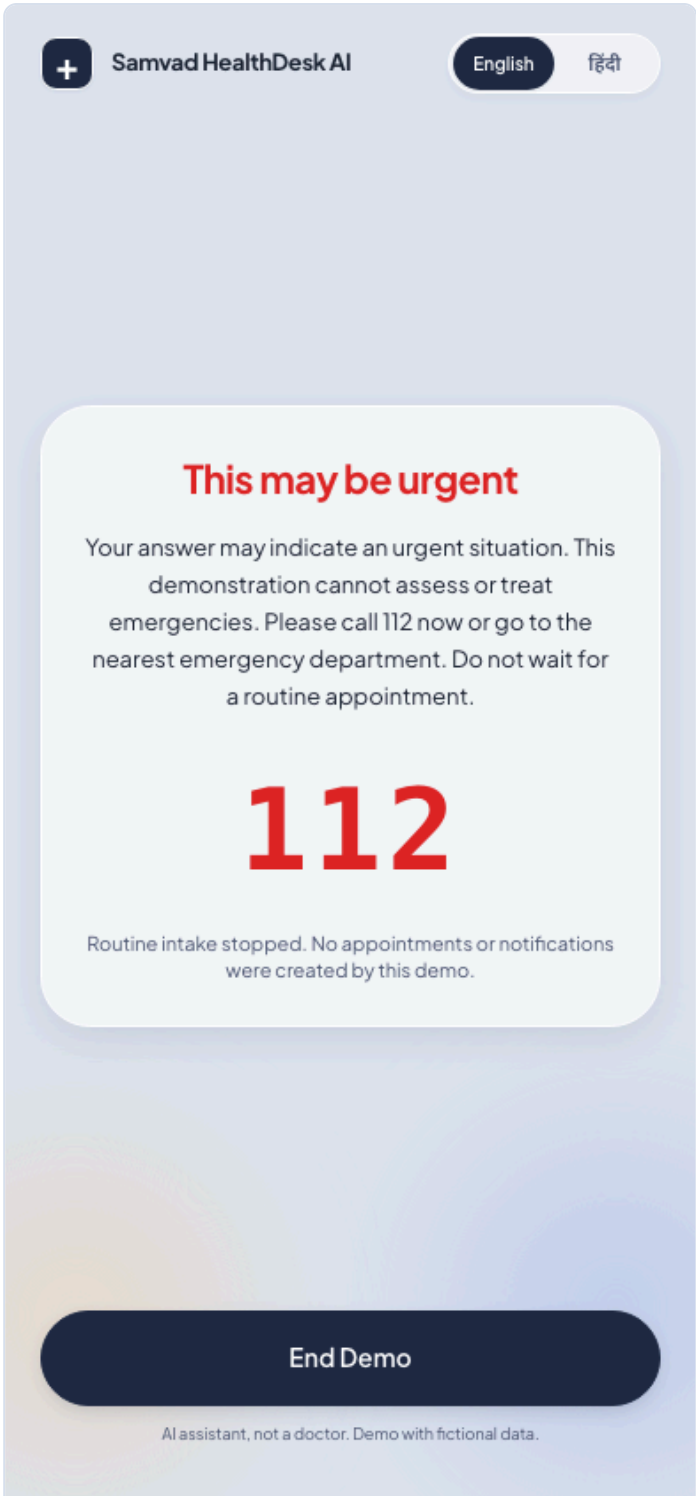


Emergency (112, no Back)

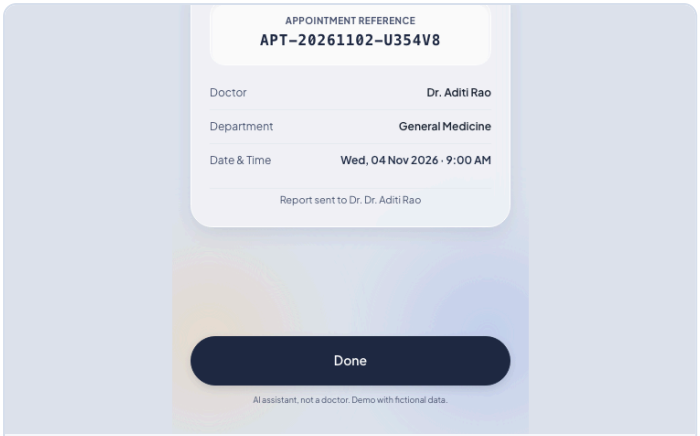


Booking confirmation (IST)

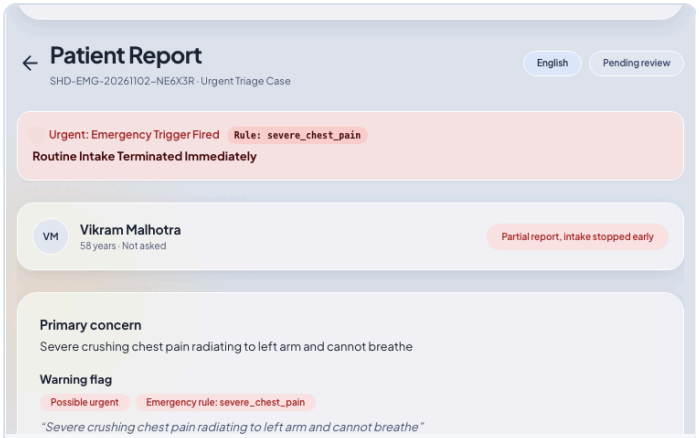


Urgent detail (real flags)

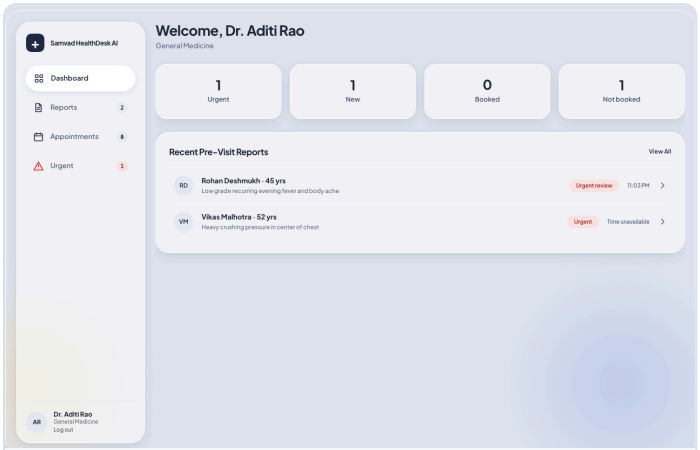


Doctor dashboard

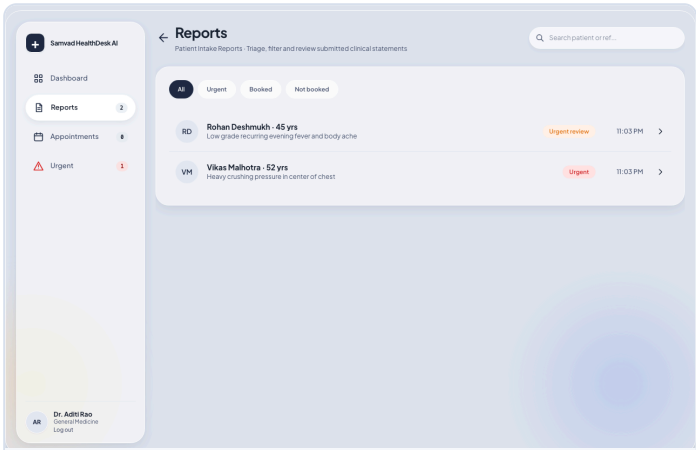


Doctor reports list

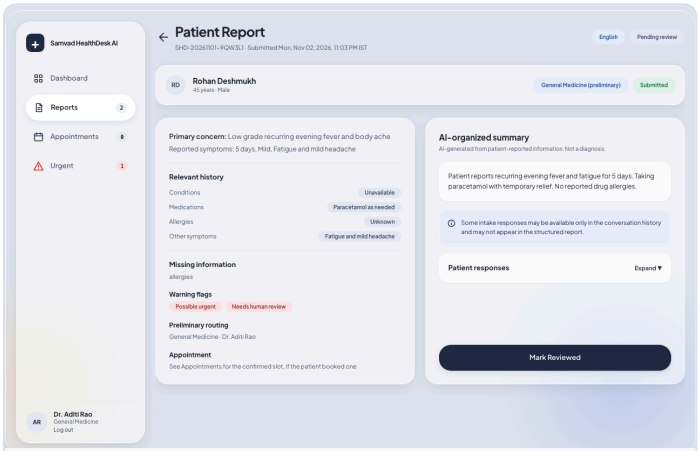


Report detail + reader

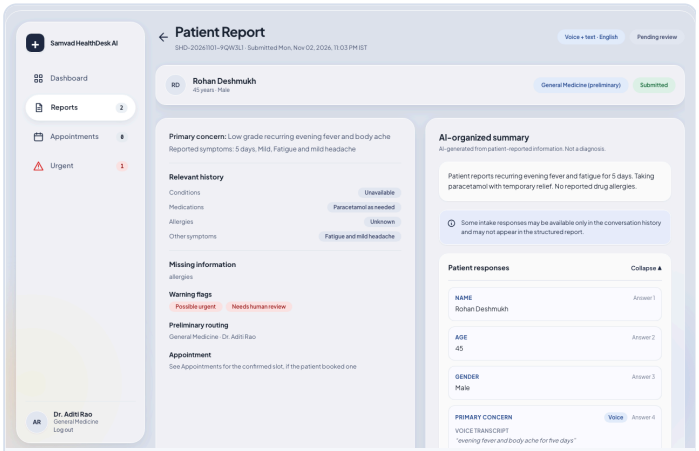

Conversation history

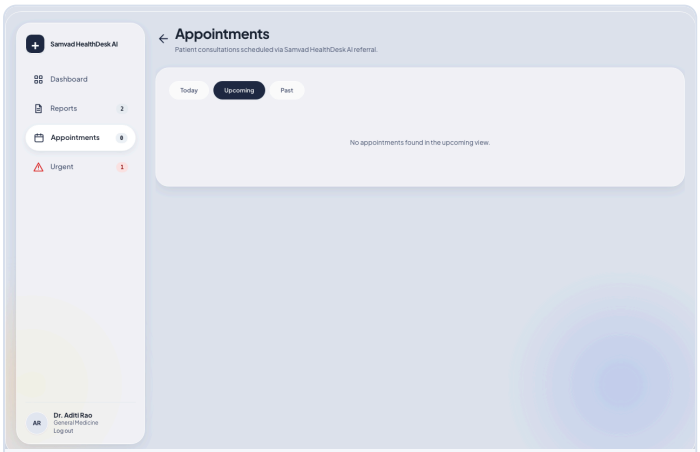

Appointments

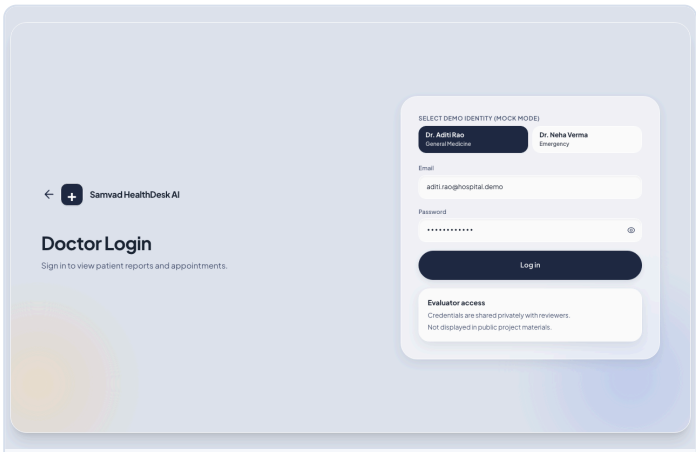

Doctor login

No API secret, key or real patient data appears in this document. All patient and doctor identities used by the application are synthetic demo data.
